


1st Ave S Reconstruction Project

E. Grant St – E. Franklin Ave.

Stakeholder Meeting
September 3rd, 2026



1st Ave S Reconstruction Project

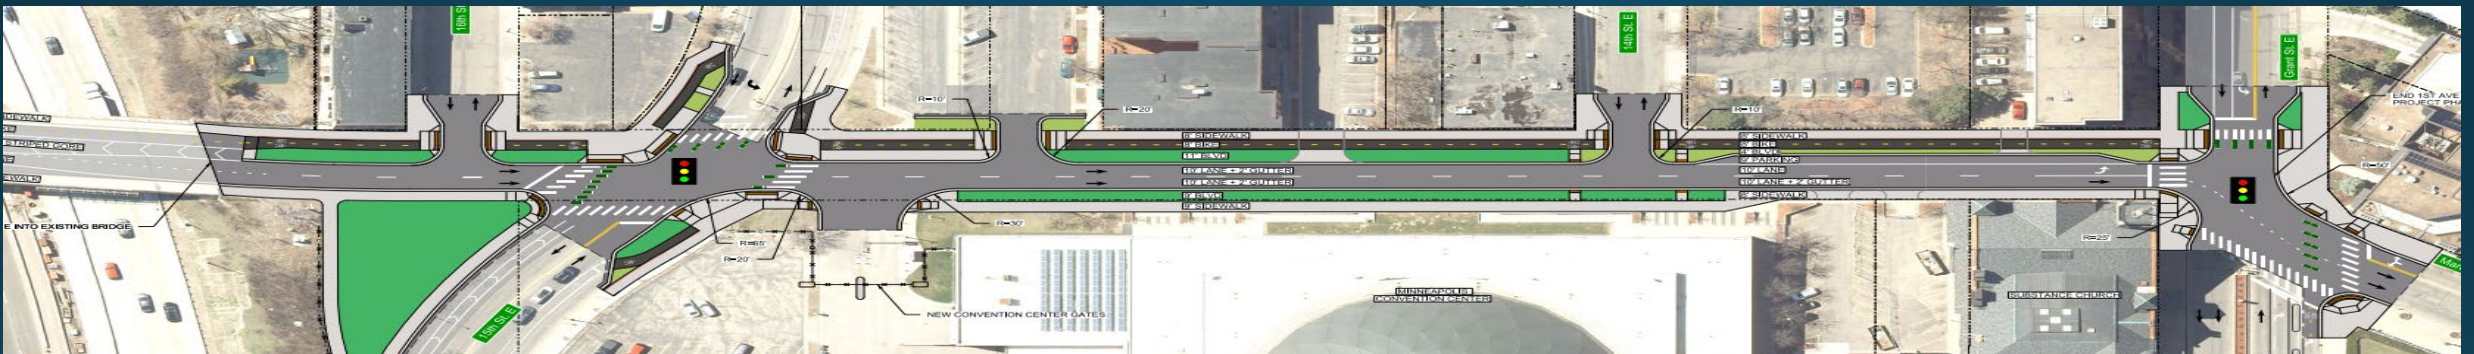

Project Layout

1st Ave S Reconstruction Project

Current Activities

City Project – Construction in progress

- Grant to 94 Bridge:
 - Surface Grading – Sidewalk
 - Concrete – Sidewalk Installation
 - Grant St. Intersection closure: August 17th, 2026 until further notice.
 - Signal System, and Sidewalk Installation
- 18th St to South of I-94 Bridge:
 - Staging & prep work – ongoing
 - Sanitary Sewer Installation
 - Storm Sewer Installation


1st Ave S Reconstruction Project

Construction- What to Expect

Roadway Construction: **In progress**

- Large Construction Equipment
- Uneven ground due to removals and utility installation
- Disruption & Noise
- Dust
- Parking Closures
- Temporary Pedestrian Ramps
- Traffic Impacts
- Business Access

Construction Substantial Completion: **November 15, 2026**

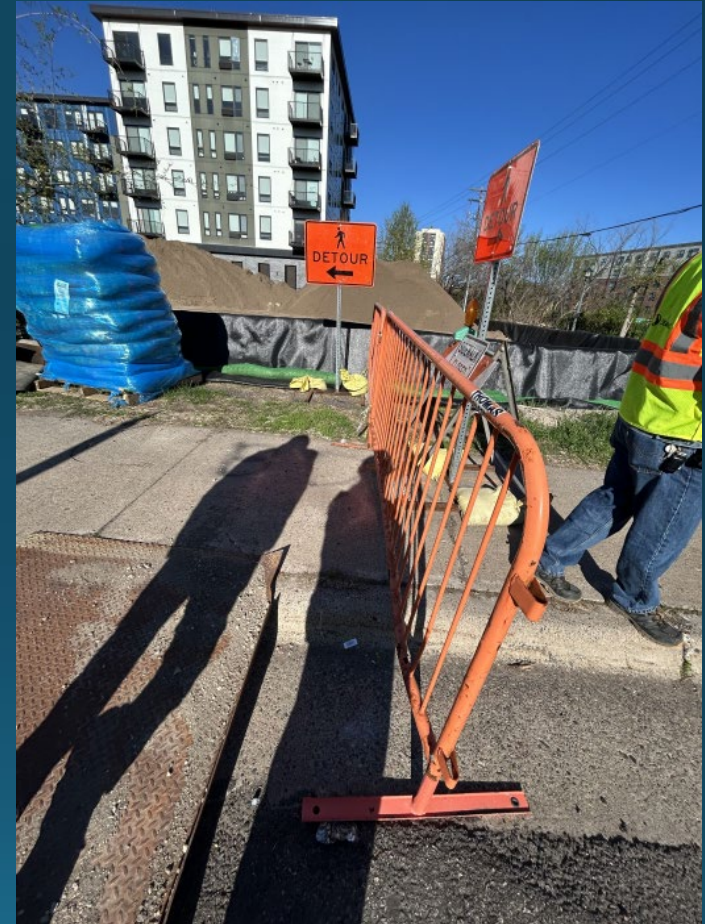

1st Ave S Reconstruction Project



South of I-94 Bridge – Sanitary Installation



Grant St – Paving

1st Ave S Reconstruction Project





18th St – Centerpoint Gas Steel Pipe Installation

1st Ave S (Grant St-Franklin Ave) reconstruction project

(Franklin Ave to 17th)

Construction progress update
September 7-11, 2026

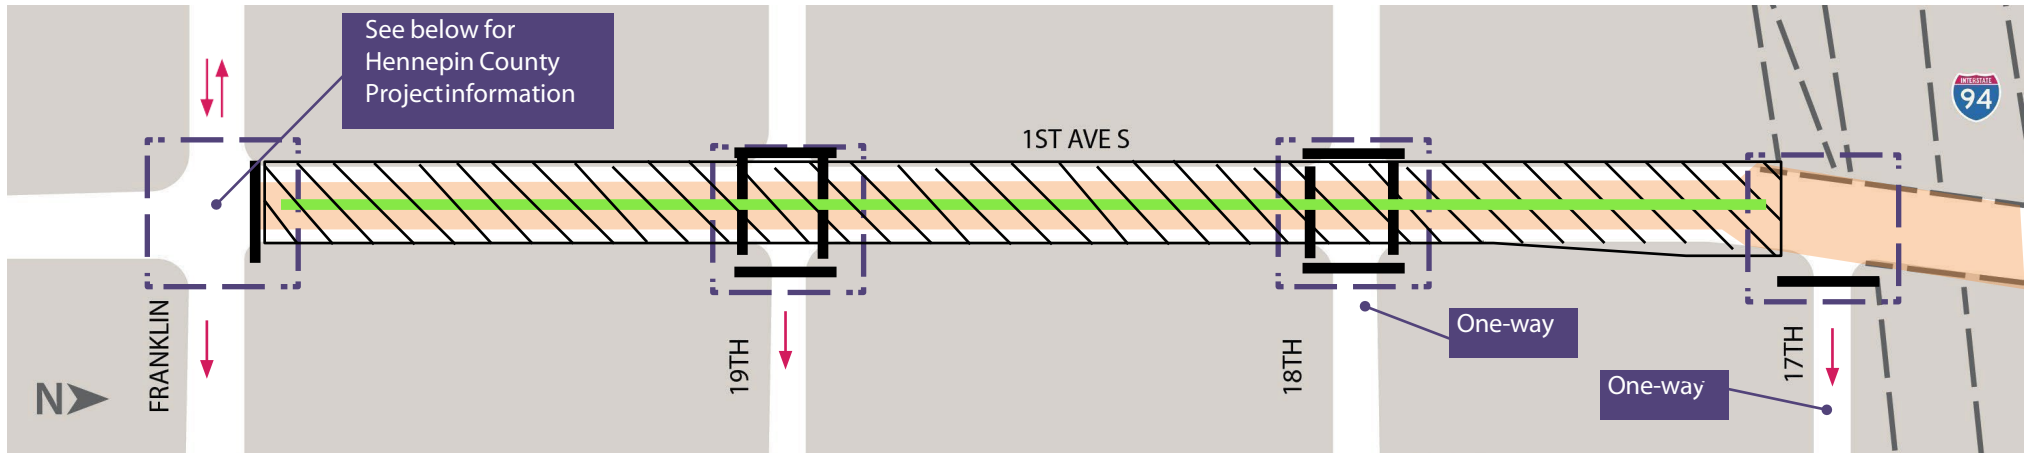

What's happening

Franklin Ave to 17th

.Franklin Ave (Hennepin County project) for more information and details visit the Franklin Ave Hennepin County project webpage:

[HennepinCounty.gov/services/roads-bridges/construction-projects/](https://hennepincounty.gov/services/roads-bridges/construction-projects/)

[franklin-avenue-reconstruction](#)

- . Centerpoint mobilization for steel pipe installation
- . Construction is ongoing with removal work.
- . Sanitary Installation
- . Storm Sewer Installation
- . Bituminous Pavement Removal



What to expect

Franklin Ave to 17th

- .Parking lanes will be closed at certain locations on sidestreets.
- .Business access will remain open during the construction.
- .Pedestrian detours will be set up as needed. Greater impacts can be expected at intersections where work is occurring.

Visit the project website
Sign up for project updates
on the project website.

[Minneapolismn.gov/
government/projects/
1st-ave-grant-st/](https://minneapolismn.gov/government/projects/1st-ave-grant-st/)



Contact us

Marian Fajutag, Construction Manager

612-834-9606 marian.fajutag@stantec.com


Rick Kreuser, Senior Construction Manager

612-770-5669 rick.kreuser@stantec.com

1st Ave S (Grant St-Franklin Ave) reconstruction project

(17th to Grant St)

Construction progress update
September 7-11, 2026

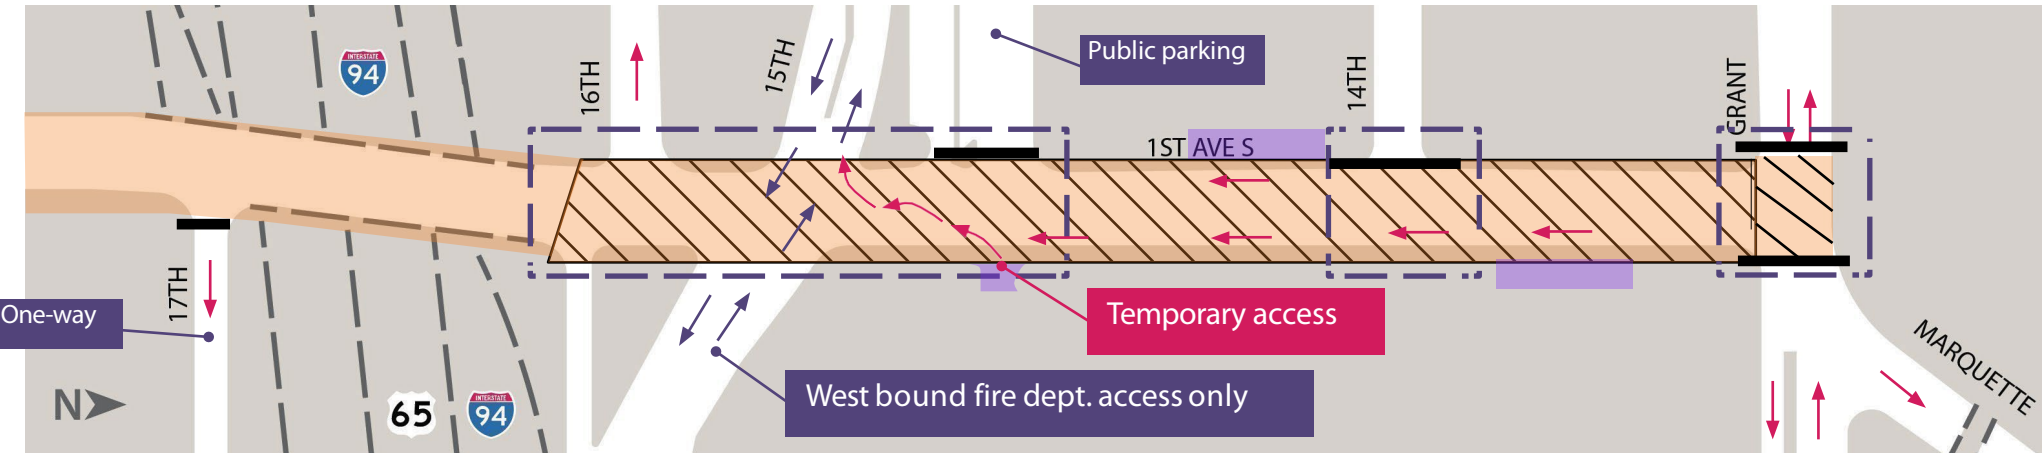

Construction work:



Partial intersection restriction



Sanitary sewer



Temporary access to parking lots



Roadway & sidewalk work

Traffic impact:



Lane closures/work zone



Travellanes



Roadway closure



What's happening

16th to Grant St

- Buses have been detoured to 15th St
- Sidewalk Preparation and Installation
- Grant St
 - Signal Systems
 - Sidewalk Preparation and Installation



What to expect

16th to Grant St

- Cross streets will be closed except for westbound access fire department, Convention Center & Stradford Flats off 15th St.
- Pedestrian detours will be set up as needed. Greater impacts can be expected at intersections where work is/
- Parking lanes will be closed at certain locations on side streets occurring. Parking will be accessible from Grant and Nicollet.
- Business access will remain open during the construction.

Visit the project website
Sign up for project updates on the project website.

[Minneapolismn.gov/government/projects/1st-ave-grant-st/](https://minneapolismn.gov/government/projects/1st-ave-grant-st/)



Contact us

Marian Fajutag, Construction Manager

612-834-9606 marian.fajutag@stantec.com

Rick Kreuser, Senior Construction Manager

612-770-5669 rick.kreuser@stantec.com

1st Ave S (Grant St-Franklin Ave) reconstruction project

(Franklin Ave to Grant St)

Construction progress update
September 7-11, 2026




Street Block	PROJECT RELATED WORK	ANTICIPATED ROAD/PEDESTRIAN RESTRICTIONS				NOTES
		TEMPORARY PEDRAMPS	PARKING RESTRICTIONS	TWO LANES OPEN	ONE LANE OPEN	
Franklin Intersection (Hennepin County Project)	Hennepin County	X	X		X	one lane open east bound and westbound
Franklin Ave-19th	Pavement Removal		X			Road closed
19th Intersection	Sanitary Sewer Installation		X			Road closed, detour via Franklin Ave
19th -18th	Sanitary Sewer Installation	X	X			Road closed, temporary pedestrian access in place
18th Intersection	Centerpoint Gas Steel Pipe Installation	X	X			Road closed, temporary pedestrian access in place
18th- 17th	Lighting; Curb and Gutter; Surface Preparation	X	X			Road closed, temporary pedestrian access in place
17th Intersection	Lighting; Curb and Gutter; Surface Preparation	X	X		X	Road closed (one-way Eastbound), temporary pedestrian access in place
17th - 16th & Bridge over I-94	No work at this time	X				Road closed, temporary pedestrian access in place.
16th Intersection	No work at this time	X	X			Intersection closed, temporary pedestrian access in place
16th- 15th	No work at this time	X	X			Road closed, temporary pedestrian access in place
15th Intersection	No work at this time	X		X		Intersection is open, temporary 4-way stop.
15th -14th	Sidewalk Preparation; Sidewalk Installation	X	X			Road closed, temporary pedestrian access in place
14th Intersection	Sidewalk Preparation; Sidewalk Installation	X	X			Road closed, temporary pedestrian access in place
14th - Grant	Sidewalk Preparation; Sidewalk Installation	X	X			Road closed, temporary pedestrian access in place
Grant Intersection	Signal System, Sidewalk Installation	X	X			Road closed, detour via 15 th St.

1st Ave S (Grant St-Franklin Ave) reconstruction project

(Franklin Ave to Grant St)

Construction progress update
September 7-11, 2026

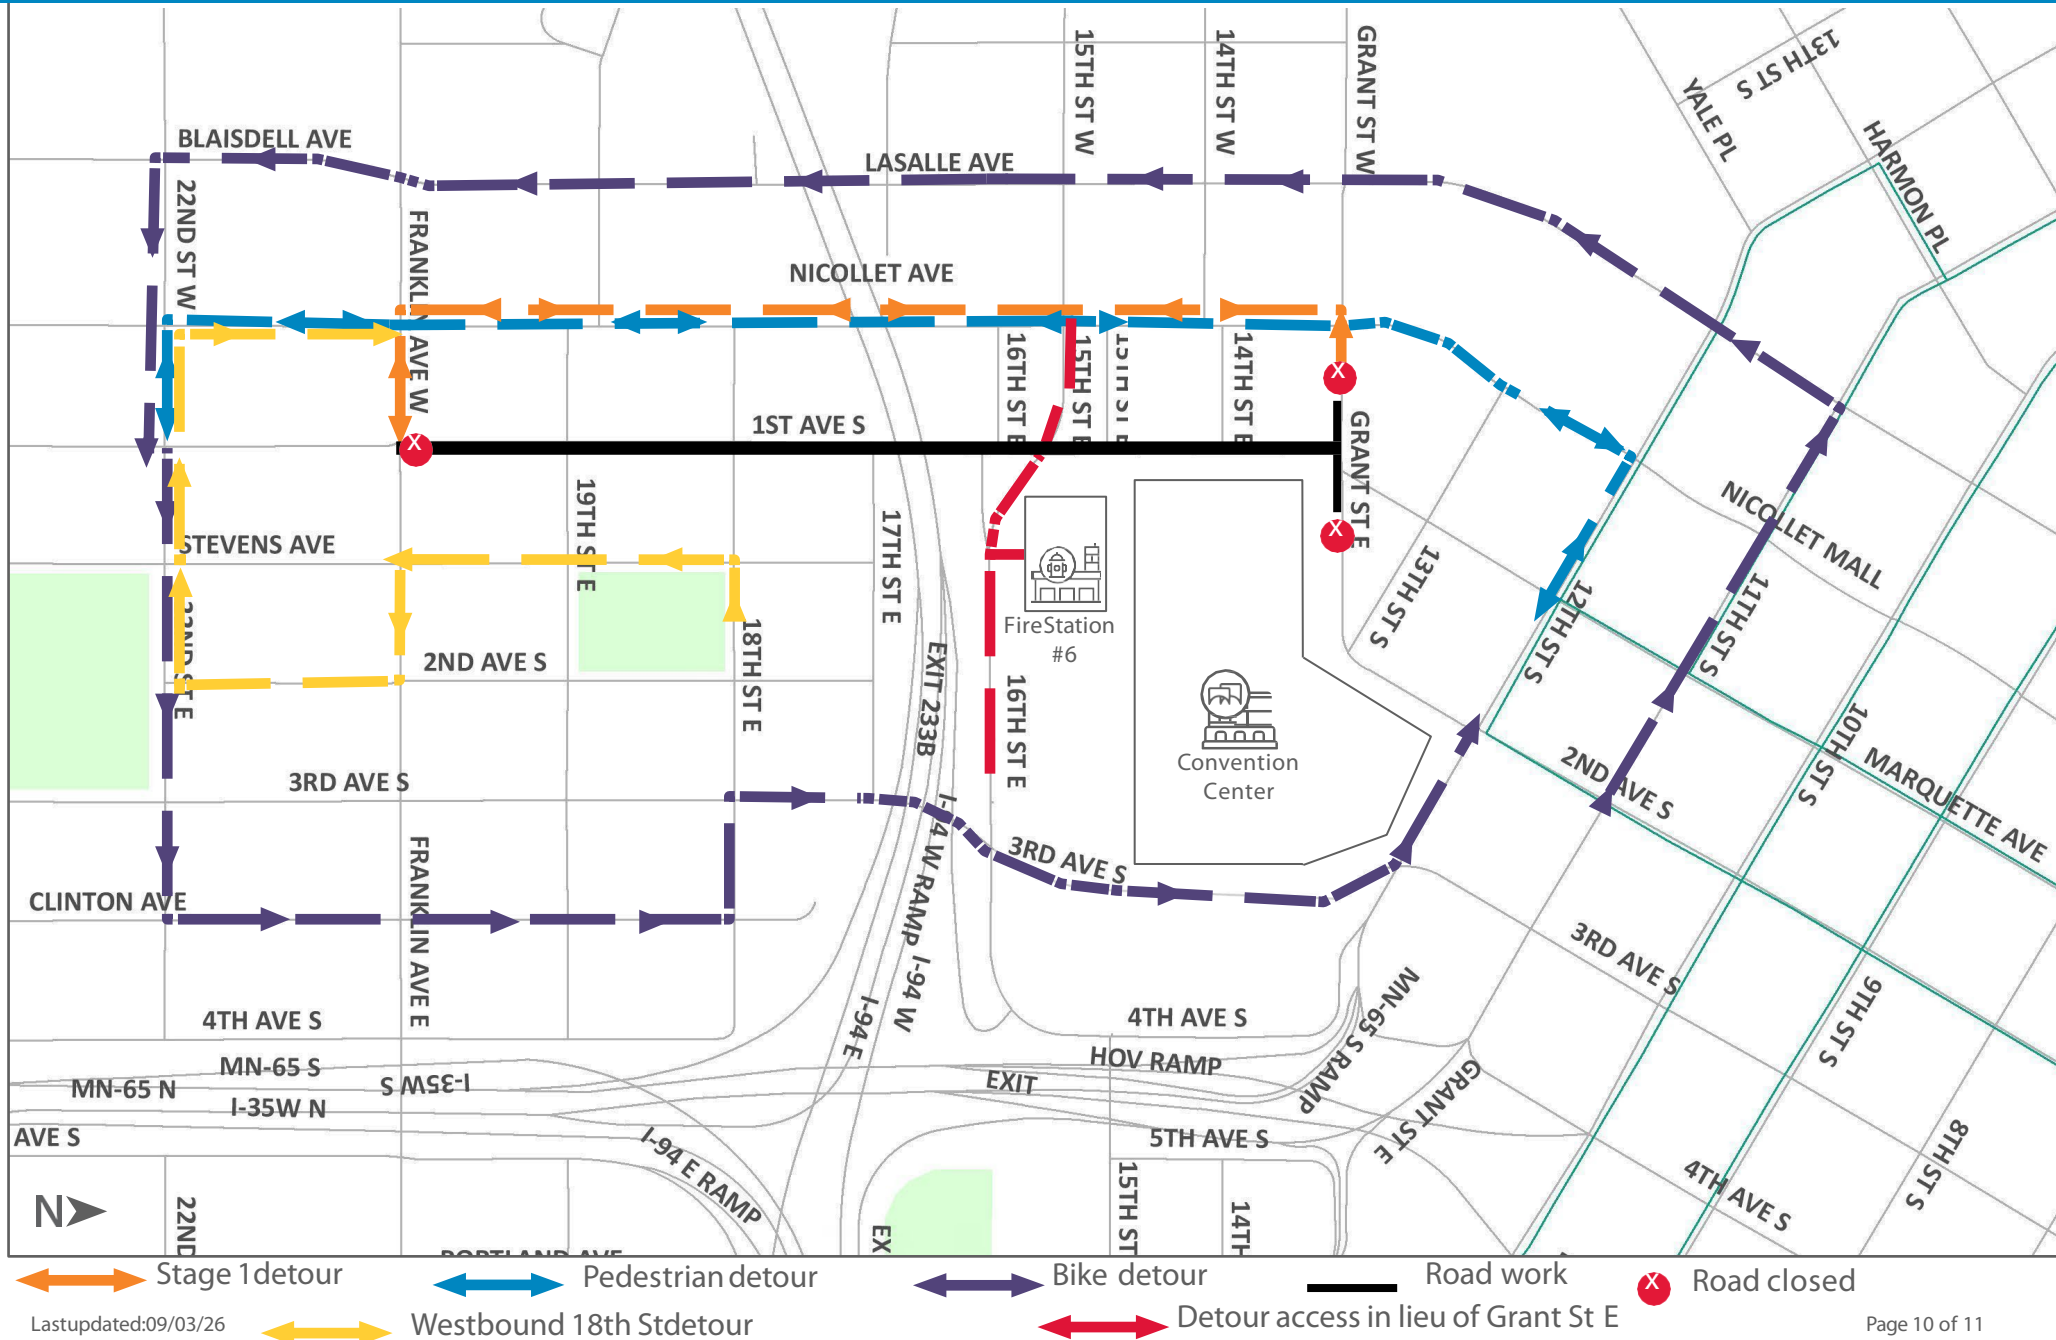


1st Ave S Reconstruction Project

Communications

- Weekly Friday Meetings 10:00 am – 11:00 am
- Weekly Email Updates (GovDelivery)
- Neighborhood Meetings
- One-on-One Site Visits
- Website – Sign up for Updates, Project Engineer & Construction Manager Contact Information

<https://www.minneapolismn.gov/government/projects/1st-ave-grant-st/>



Contact us

Marian Fajutag, Construction Manager

📞 612-834-9606 📧 marian.fajutag@stantec.com

Rick Kreuser, Senior Construction Manager

📞 612-770-5669 📧 rick.kreuser@stantec.com

