



The Lasalle Avenue Project

Volume 1 04.04.14

Lasalle Avenue from 8th Street to Grant Street


- MAJOR UTILITY WORK - 2014**
- CenterPoint Gas Main Replacement
 - CenterPoint Maintenance/Service Work
 - Minneapolis Water Main Replacement
 - Xcel Energy Duct Line Replacement
 - Xcel Energy Manhole Replacement/Repair Work
 - Century Link Duct Line Replacement
 - NRG Vault Expansion and Line Replacement
- Mill and Overlay (2014)
- Paving Reconstruction (2015)

ADDITIONAL UTILITY WORK - BY OTHERS

- Comcast
- Sprint
- Windstream
- Minneapolis Surface Water & Sewers
- Minneapolis Traffic

CONSTRUCTION FOR THE WEEK OF APRIL 7-11

- Minneapolis water installing valves. Lane closures on the north side of 10th Street.
- NRG repair of leaking pipe. Lane restriction on Lasalle north of 11th Street.

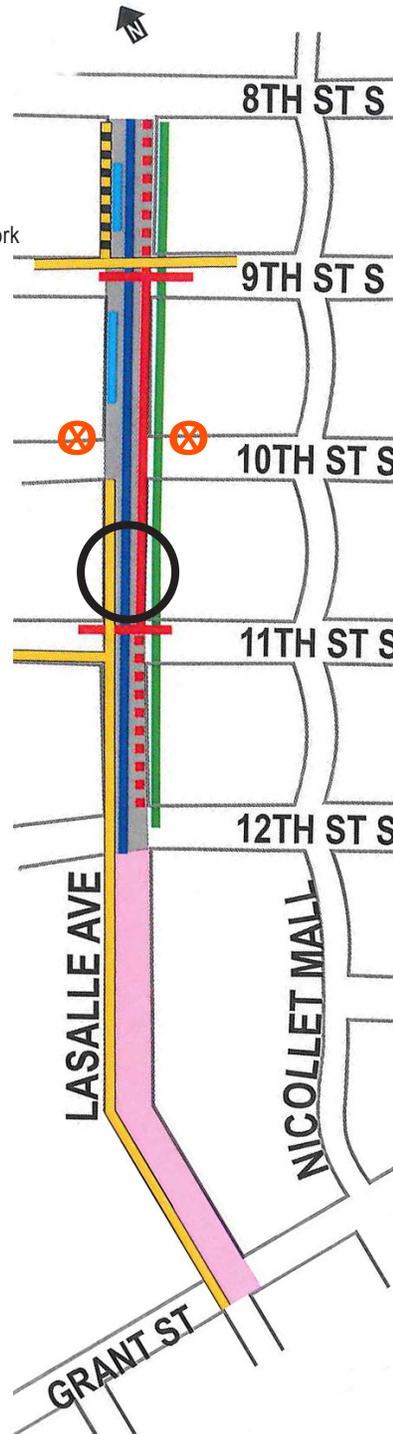

The City of Minneapolis is in the process of preparing final plans for the repair and/or reconstruction of Lasalle Avenue from 8th Street to Grant Street. The plans are for a mill and overlay on the segment from 12th Street to Grant Street and a complete reconstruction of the street from 8th Street to 12th Street.

Our planning for any project like this includes a review of all of the underlying public and private utility systems and the coordination of any repairs, replacements, or upgrades to these systems that may be necessary.

The existing condition of the segment of roadway from 12th Street to Grant Street, together with a minimal requirement to disrupt the existing street for utility work allows us to improve the current condition of this portion of the roadway with a mill and overlay. This work is scheduled for this year (2014).

The existing condition of the segment from 8th Street to Grant Street, together with the need to remove the majority of the existing street for utility work makes it more cost effective for us to plan for a complete reconstruction of this segment. In 2014 we will be coordinating all of the necessary utility improvements in this segment and providing temporary surface repairs to the street as work is completed.

Some preliminary utility work has started this week. The level of utility construction work will continue to increase over the next few weeks as more companies begin work.

With the utility work completed in 2014 the reconstruction work of the roadway from 8th Street to 12th Street is scheduled to be done during the first half of the 2015 construction season.

We will provide weekly updates of project activity each Friday with more specific information as plans are completed. We thank you in advance for your patience and cooperation.

