


E 26th St and Hiawatha Intersection Improvements

(E 26th St to Hiawatha Ave)

Construction progress update
September 13 - September 19, 2026

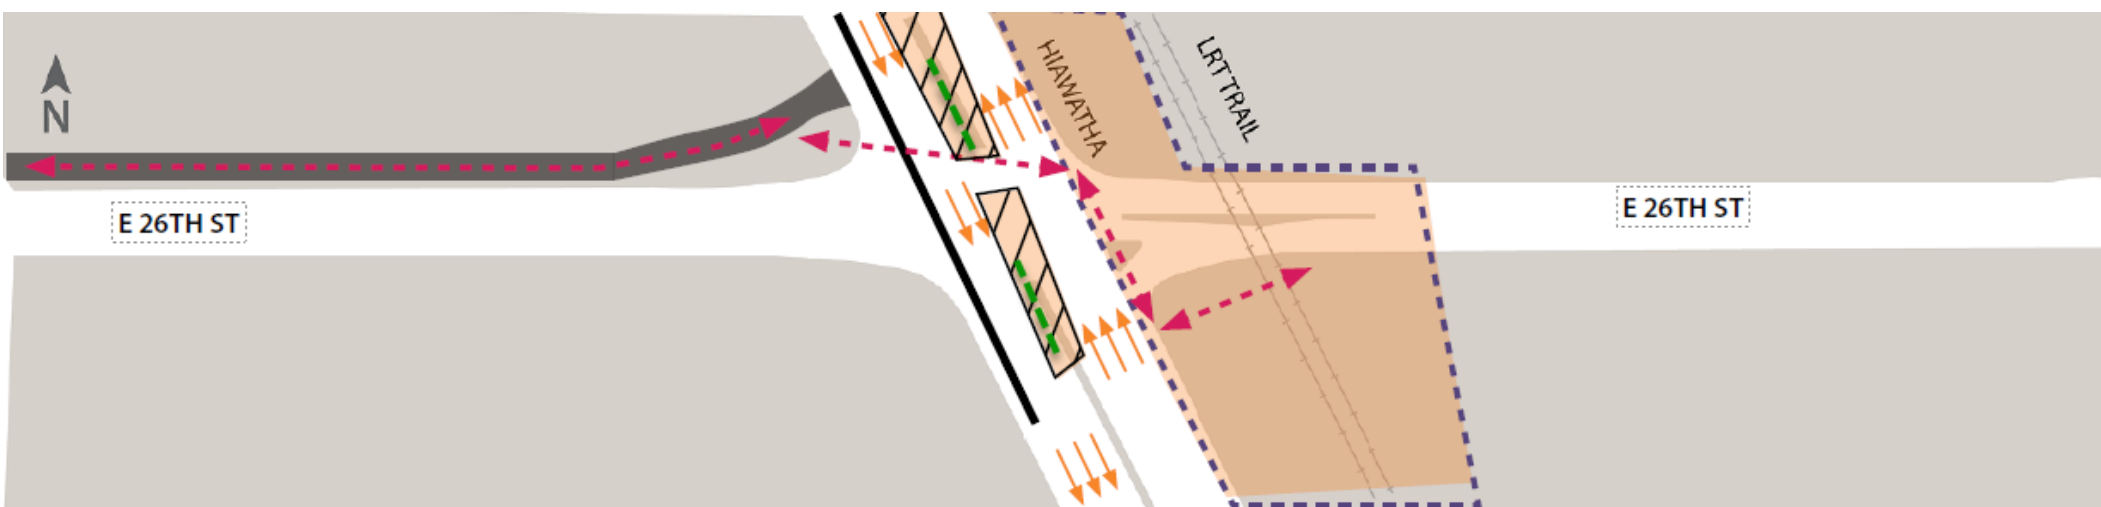

Construction work:



Partial Intersection Restriction



Shared-use trail

Conduit work

Local ped/bike detour

Traffic impact:



Lane Closures/Work Zone



Travel Lanes



Roadway Closure



Roadway & Sidewalk work



What's happening

E 26th St & Hwy 55

- Concrete pavement and curb and gutter patches at E 26th Street and Hiawatha Ave
- General site cleanup



What to expect

E 26th St & Hwy 55

- Roadway and utility work will continue on the E. side of Hiawatha and E 26th Street.
- Access to Jefferson Lines will be maintained during construction.
- Pedestrian detours will be set up as needed. Greater impacts can be expected at intersections where work is occurring.
- Pedestrian ramps in the median areas are expected to be completed next week
- Signing and striping on Hiawatha Ave is expected the week of September 21st.
- For Light Rail Transit corridor safety, the east side of the intersection at E 26th Street and Hiawatha will remain closed until the permanent signal poles are received. These are anticipated to arrive this fall.



Stay connected

Visit the project website

Sign up for project updates on the project website.

[Minneapolismn.gov/
government/projects/
26th-hiawatha-safety/](https://minneapolismn.gov/government/projects/26th-hiawatha-safety/)



Contact us

Steven Kroening, Chief Field Inspector - Public Works

612-246-8553 steven.kroening@minneapolismn.gov


Kyle Wallace, Project Manager - Public Works

612-673-2438 kyle.b.wallace@minneapolismn.gov

E 26th St and Hiawatha Intersection Improvements

(E 26th St to Hiawatha Ave)

Construction progress update
September 13 - September 19, 2026

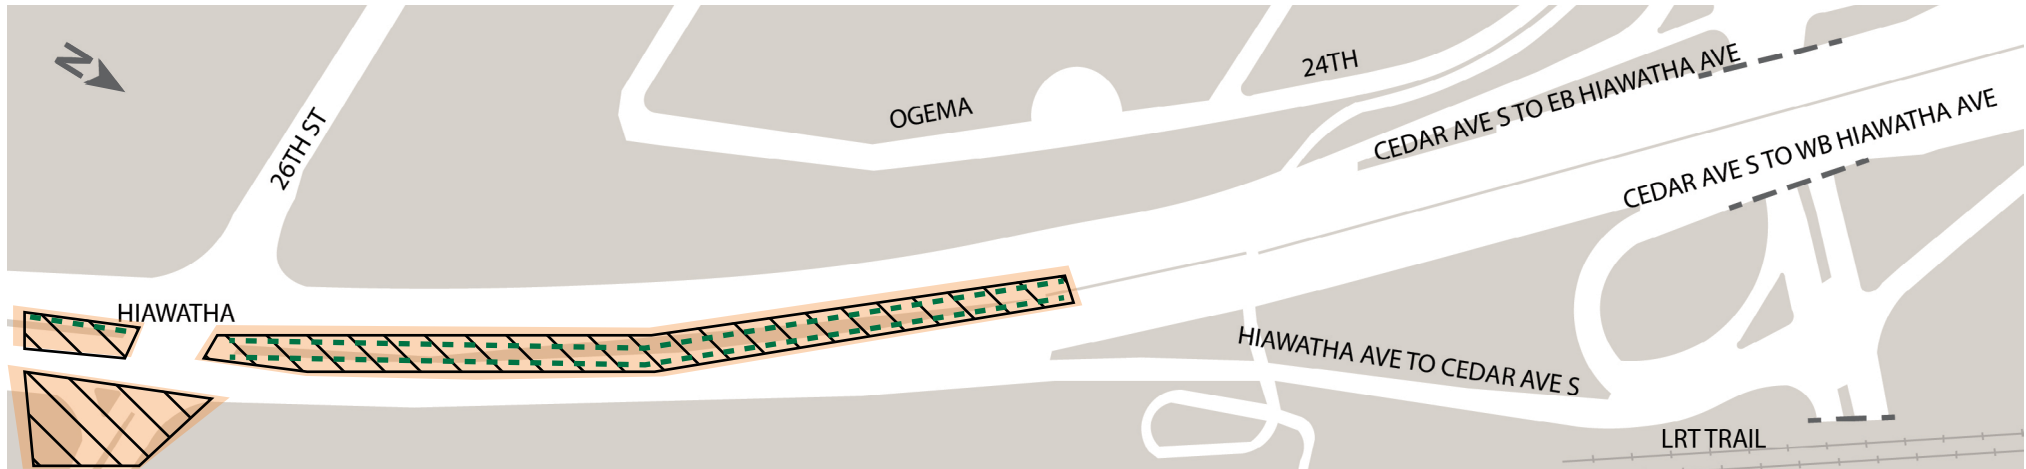

Construction work: Partial Intersection Restriction Sanitary Sewer Conduit Work Storm Sewer

Traffic impact: Lane Closures/Work Zone Travel Lanes Roadway Closure Roadway & Sidewalk work



What's happening

Hiawatha Ave

- Joint preparation for hot seal was completed this week.
- Pavement joint sealing is expected next week.



What to expect

Hiawatha Ave

- New pavement markings and signing is expected next week. (weather permitting)



Stay connected

Visit the project website

Sign up for project updates on the project website.

[Minneapolismn.gov/
government/projects/
26th-hiawatha-safety/](https://minneapolismn.gov/government/projects/26th-hiawatha-safety/)



Contact us

Steven Kroening, Chief Field Inspector - Public Works

📞 612-246-8553 📧 steven.kroening@minneapolismn.gov

Kyle Wallace, Project Manager - Public Works

📞 612-673-2438 📧 kyle.b.wallace@minneapolismn.gov
