Gantt Chart

		Task Name	Duration	Start	Finish	Predece	Resource N
1		Flood Area 27 and 28th Ave reconstruction	0 days	Tue 1/24/06	Tue 1/24/06		
2		**Council/Resident**	**71 days**	**Tue 1/24/06**	**Tue 5/2/06**		
3	✓	T&PW letter	1 day	Tue 1/24/06	Tue 1/24/06		
4	✓	T&PW committee	1 day	Tue 1/31/06	Tue 1/31/06		
5	✓	Mail notice for public meeting	12 days	Wed 2/1/06	Thu 2/16/06	4	
6	✓	Public Meeting	9 days	Fri 2/17/06	Wed 3/1/06	5	
7		T&PW letter for assessment	1 day	Mon 3/13/06	Mon 3/13/06		
8		Assessment hearing at T&PW	1 day	Tue 5/2/06	Tue 5/2/06		
9		**Plans for 28th Ave Reconstruction**	**47 days**	**Tue 3/7/06**	**Wed 5/10/06**		
10	✓	90% plans redone	20 days	Tue 3/7/06	Mon 4/3/06		
11	✓	CPTF 90%	1 day	Mon 4/3/06	Mon 4/3/06		
12		Final plans	19 days	Tue 4/4/06	Fri 4/28/06	11	
13		Final quantities	1 day	Mon 5/1/06	Mon 5/1/06	12	
14		Final cost estimate	1 day	Mon 5/1/06	Mon 5/1/06	12	
15		Plans for city signatures	7 days	Tue 5/2/06	Wed 5/10/06	14	
16		**FA 27 sewer construction**	**105 days**	**Tue 3/7/06**	**Mon 7/31/06**		
17	✓	Establish current schedule	1 day	Tue 3/7/06	Tue 3/7/06		
18	✓	Resident notification letter	2 days	Tue 3/7/06	Wed 3/8/06		
19	✓	Traffic control devices	3 days	Thu 3/9/06	Mon 3/13/06	18	
20		Box culvert 39th to 40th	45 days	Tue 3/14/06	Mon 5/15/06	19	
21		Box culvert 38th to 39th	55 days	Tue 5/16/06	Mon 7/31/06	20	
22		**28th Ave street reconstruction**	**85 days**	**Tue 5/16/06**	**Mon 9/11/06**		
23		Street reconstruction 39th to 40th	25 days	Tue 5/16/06	Mon 6/19/06	20	
24		Street reconstruction 38th to 39th	25 days	Tue 8/1/06	Mon 9/4/06	21	
25		boulevard sod	5 days	Tue 9/5/06	Mon 9/11/06	24	
26		**Seal coat aggregate**	7 days	Mon 7/2/07	Tue 7/10/07		

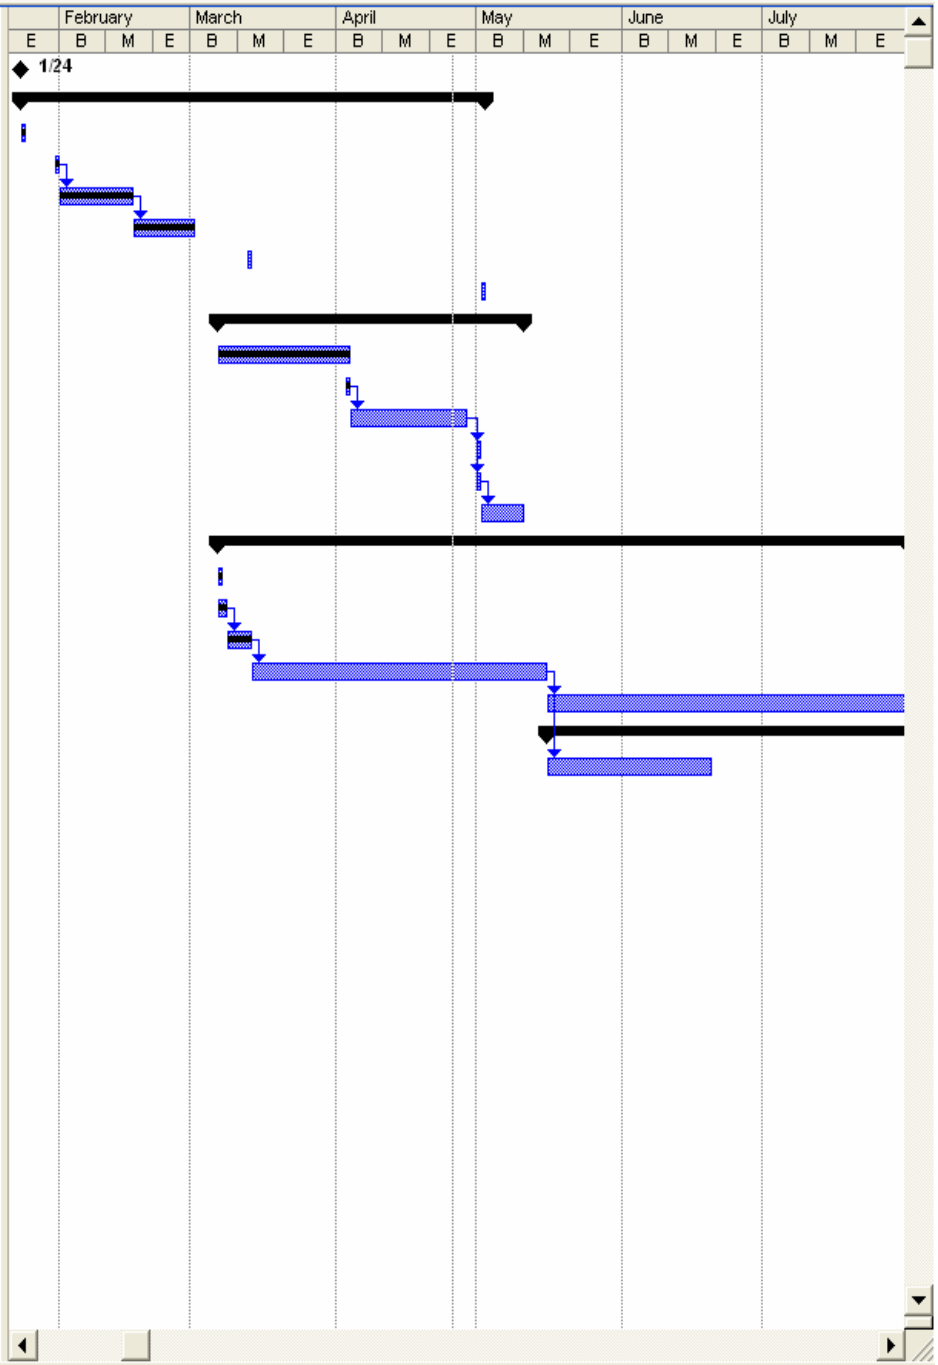

Ready
