

Nicollet Avenue Reconstruction

Public Information Meeting
March 26, 2013



Minneapolis
City of Lakes



Agenda/Meeting Purpose

- **Project Overview**
- **2012 Construction**
- **2013 Construction**
 - **Phasing/Staging**
 - **What to expect**
 - **Contacts**
- **Questions**



Project Overview

- **Roadway Reconstruction**
 - **44' Roadway with Transition Areas**
 - **Lake Street to 31st Street**
 - **36th Street Intersection**
 - **38th Street Intersection**
 - **5' Boulevards with new trees**
 - **New 6' Sidewalks**
 - **New Storm Sewer**
 - **Repair Water Main and Sanitary Sewer**
 - **Traffic Signal Upgrades**
 - **Refurbished lighting system**



2012 Construction


- **Substantially complete from Lake St to 36th St**
 - **Edge line striping installed spring/summer 2013**
 - **Trees to be installed in the fall planting season**
 - **Nicollet Ave/36th St signal completed spring 2013**
 - **Public Arts administrator is working with property owners to determine locations for public art**

Nicollet Avenue Reconstruction



Minneapolis
City of Lakes

2012 Construction

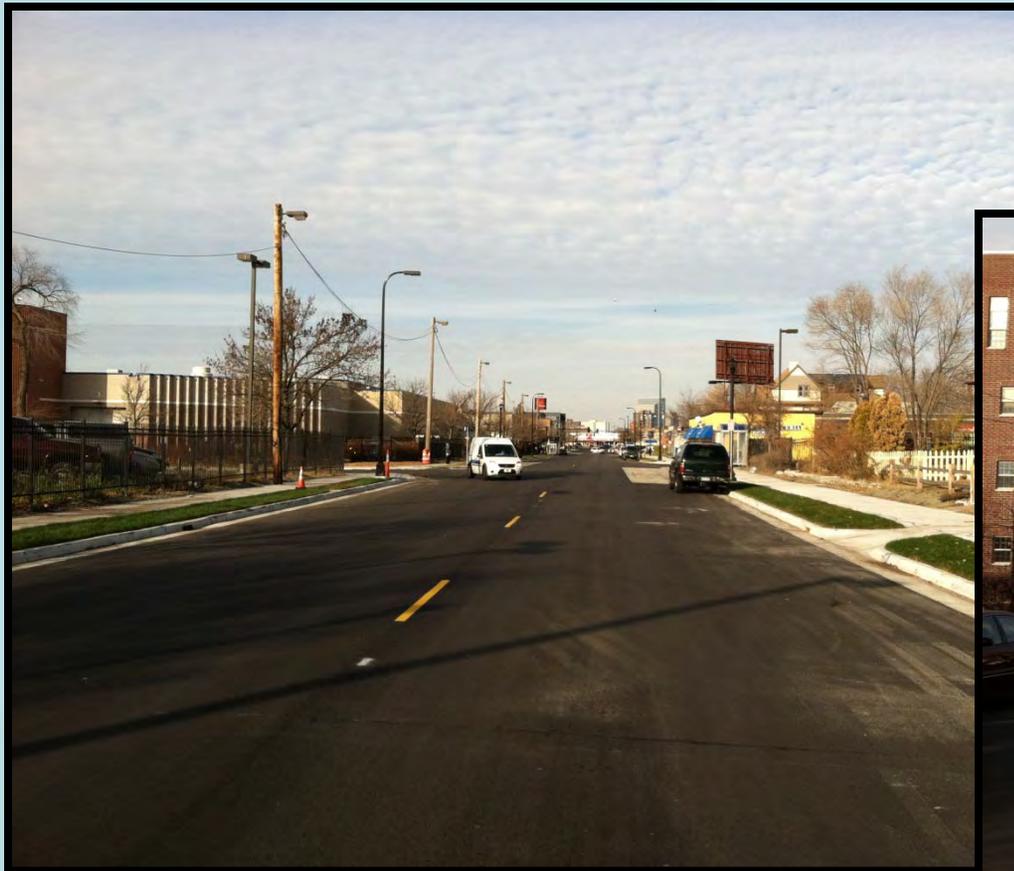



2012 Construction

- **Lessons Learned**
 - **What Went Well**
 - Full-time on-site inspector was valuable
 - Email updates effective in providing timely information
 - 1-3 block segments worked well to minimize direct impacts to properties
 - **What Can Be Improved**
 - Pedestrian access through construction zone
 - Timeliness of updates to access signing
 - Coordination with utilities



2013 Construction

- **Phasing/Staging**
 - **Phase 1 - 36th Street to 38th Street**
 - Includes Nicollet Ave/38th St intersection
 - 36th St and 38th St intersections remain open
 - Anticipated to start April 2013





2013 Construction


- **Phasing/Staging**
 - **38th Street to 40th Street**
 - Includes Nicollet Ave/40th St intersection
 - 38th St and 40th St intersections remain open
 - Tentatively scheduled to start August 2013





2013 Construction

- Nicollet Ave will be open to traffic outside the construction zone
- Access to businesses and driveways maintained
- Bus detour will be the same as traffic detour
 - Bus stops will be on 1st Ave and Blaisdell Ave

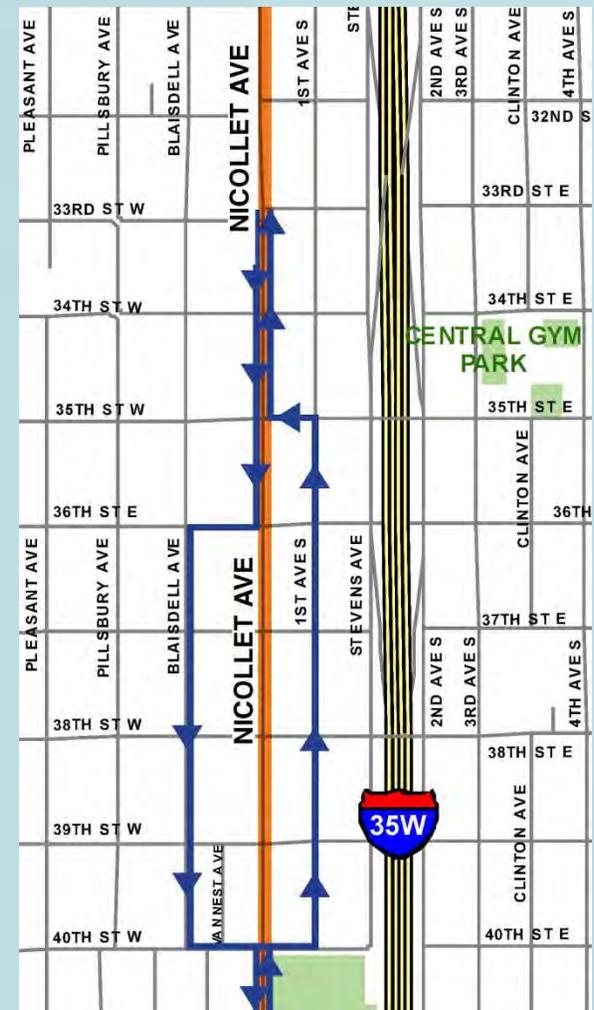



2013 Construction

- **Construction hours will generally be 7am to 6pm weekdays**
 - **Night or weekend work may be needed**
- **Temporary water main**
- **Coordination with 38th St resurfacing**
 - **38th St resurfacing project intended to be completed late April**

Nicollet Avenue Reconstruction



Minneapolis
City of Lakes





2013 Construction

- **Contacts**

- **On-Site Issues, 24-Hours - Bob Schmidt**
651-308-3805

- **Public Works – Bev Warmka 612-673-3762**

- **Email updates**

- **Subscribe at**

- https://public.govdelivery.com/accounts/MPLS/subscriber/new?topic_id=MPLS_169**

Nicollet Avenue Reconstruction



Minneapolis
City of Lakes

Questions?
